

5/110 STATION ROAD, SEVEN HILLS NSW 2147
Ph: 02 9838 4735 Fax: 02 9838 4710

VISUAL INSPECTION REPORT

Customer	: RAR GROUP	Contact	: PAT
Location	: U 924	Date Inspected	: 04.02.2025
D/D No	: N/A	Report No	: 222183
Report Received by	: pat@rargroup.com.au	Customer O/N	: ANNUAL
Next Inspection Due	: FEB 2025	Colour Code	: RED

This report follows the visual inspection of lifting gear at your facility by Matthew Lovett-Jeans. Inspections were conducted with reference to Company endorsed Work Instructions, Relevant Standards, Occupational Health & Safety requirements and Manufacturers recommendations to determine acceptance / rejection criteria's.

1. AS3776-2006 LIFTING COMPONENTS FOR GRADE T CHAIN
2. AS3775.1-2014 CHAIN SLINGS GRADE T

All items satisfying the above requirements were tagged or hard stamped to cross reference with this report.

Items listed as "R" (Repair) should be quarantined and repaired prior to further use.

Items listed as "F" (Fail) are not suitable for continued use or for their intended purpose and should be destroyed and discarded immediately. We cannot accept any responsibility for continued use

Items listed as "N" (Not Presented) were unable to be located on site.

Items listed as "P" (Pass) are suitable for continued use and can be put back into service. Should any replacement parts be required they can be supplied by reference to the item number of this report.

All items have been fitted with a **RED** colour coded identification tag. We shall contact you early FEBRUARY to arrange your next inspection. Should you require any further information please contact the undersigned.

Yours Truly.



Matthew Lovett-Jeans
Inspection Officer
Email: sydneyinspections@alllifting.com.au
Phone: 02 9838 4735


Report No:222183

Customer Name: RAR GROUP

Date of Inspection: 04.02.2025

Item	Identification Number	Description	W.L.L. Or D.O.W	Location	Inspection Date	Inspection Due	Comments	P / F / R / N
1	K294	8MM GRADE 100 2 LEG ASSEMBLY COMPLETE WITH LARGE MULTI LINK, EYE GRABS AND CLEVIS SELF LOCKING HOOKS AT BASE. 8M	4.3 TONNE @ 60 DEG	924	4.02.2025	FEB 2025	N/A	Pass
2	K293	8MM GRADE 100 2 LEG ASSEMBLY COMPLETE WITH LARGE MULTI LINK, EYE GRABS AND CLEVIS SELF LOCKING HOOKS AT BASE. 8M	4.3 TONNE @ 60 DEG	924	4.02.2025	FEB 2025	N/A	Pass
3	3138	8MM GRADE 80 2 LEG ASSEMBLY COMPLETE WITH OBLONG LINK, EYE GRABS AND CLEVIS SELF LOCKING HOOKS AT BASE. 8M	3.5 TONNE @ 60 DEG	924	4.02.2025	FEB 2025	N/A	Pass
4	P3102	10MM GRADE 80 2 LEG ASSEMBLY COMPLETE WITH EYE GRABS AND CLEVIS SELF LOCKING HOOKS AT BASE.	5.5 TONNE @ 60 DEG	924	4.02.2025	FEB 2025	N/A	Pass
5	J476	10MM GRADE 80 2 LEG ASSEMBLY COMPLETE WITH EYE GRABS AND CLEVIS SELF LOCKING HOOKS AT BASE.	5.5 TONNE @ 60 DEG	924	4.02.2025	FEB 2025	N/A	Pass
6	J418	10MM GRADE 80 2 LEG ASSEMBLY COMPLETE WITH EYE REGULAR MULTI LINK, EYE GRABS AND CLEVIS SELF LOCKING HOOKS AT BASE.	5.5 TONNE @ 60 DEG	924	4.02.2025	FEB 2025	N/A	Pass
7	192452	8MM GRADE 100 2 LEG ASSEMBLY COMPLETE WITH LARGE MULTI LINK, EYE GRABS AND CLEVIS SELF LOCKING HOOKS AT BASE. 8M	4.3 TONNE @ 60 DEG	924	4.02.2025	FEB 2025	N/A	Pass
8	KA22	10MM KUPLEX MULTI LINK G100	6.9 TONNE @ 60 DEG	924	4.02.2025	FEB 2025	N/A	Pass

1300 666 733 • www.allifting.com.au

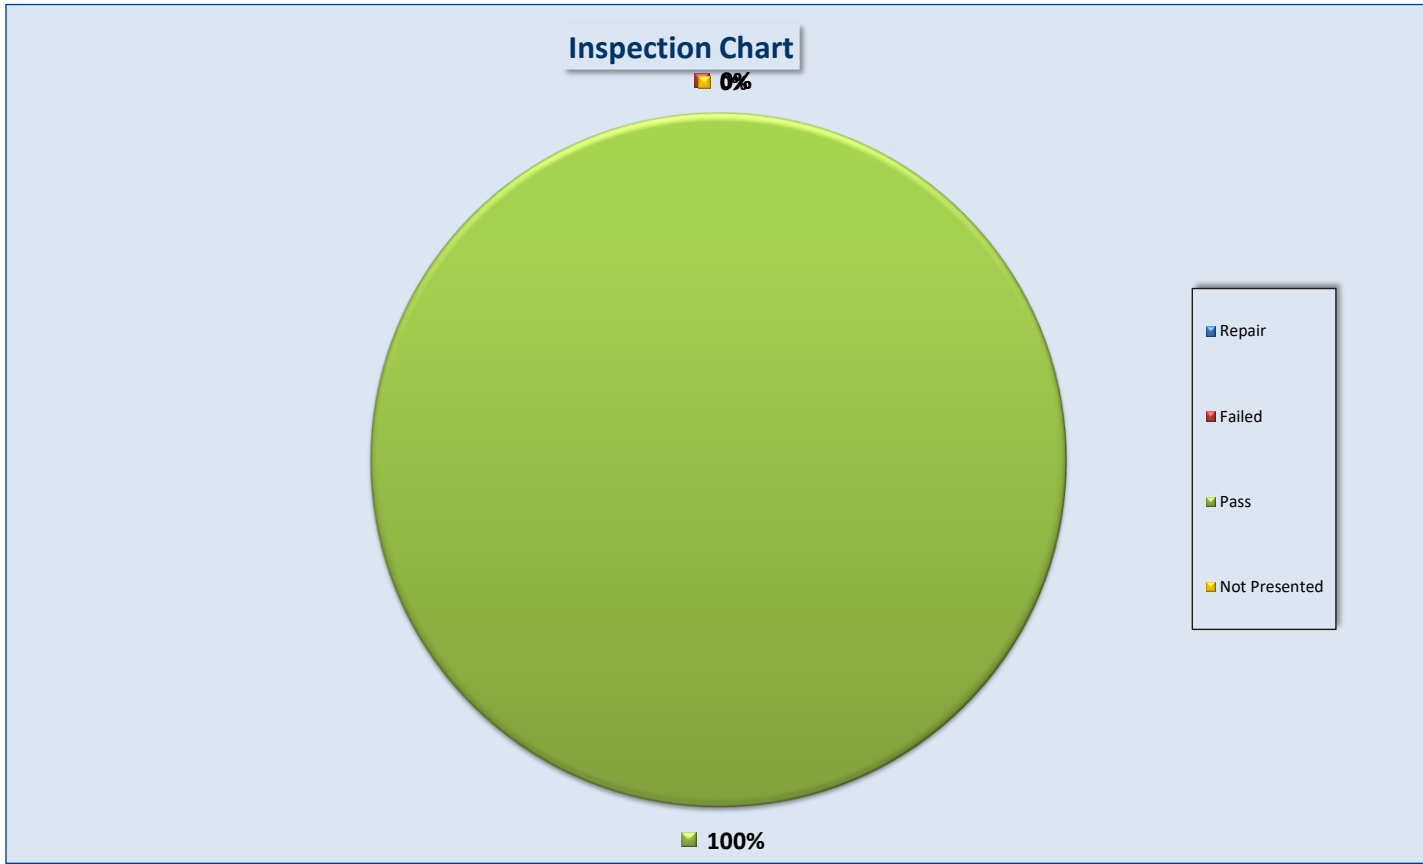

Report No:222183	
Repair	
Failed	
Pass	8
Not Presented	
TOTAL	8
