



5/110 STATION ROAD, SEVEN HILLS NSW 2147
Ph: 02 9838 4735 Fax: 02 9838 4710

VISUAL INSPECTION REPORT

Customer	: RAR GROUP	Contact	: PAT
Location	: U 941	Date Inspected	: 03.02.2025
D/D No	: N/A	Report No	: 222183
Report Received by	: pat@rargroup.com.au	Customer O/N	: ANNUAL
Next Inspection Due	: FEB 2026	Colour Code	: RED

This report follows the visual inspection of lifting gear at your facility by Matthew Lovett-Jeans. Inspections were conducted with reference to Company endorsed Work Instructions, Relevant Standards, Occupational Health & Safety requirements and Manufacturers recommendations to determine acceptance / rejection criteria's.

1. AS4497.2-1997 ROUND SLINGS
2. AS3775.1-2014 CHAIN SLINGS GRADE T

All items satisfying the above requirements were tagged or hard stamped to cross reference with this report.

Items listed as "R" (Repair) should be quarantined and repaired prior to further use.

Items listed as "F" (Fail) are not suitable for continued use or for their intended purpose and should be destroyed and discarded immediately. We cannot accept any responsibility for continued use

Items listed as "N" (Not Presented) were unable to be located on site.

Items listed as "P" (Pass) are suitable for continued use and can be put back into service. Should any replacement parts be required they can be supplied by reference to the item number of this report.

All items have been fitted with a **RED** colour coded identification tag. We shall contact you early FEBRUARY to arrange your next inspection. Should you require any further information please contact the undersigned.

Yours Truly,

Matthew Lovett-Jeans
Inspection Officer
Email: sydneyinspections@alllifting.com.au
Phone: 02 9838 4735




Report No:222183

Customer Name: RAR GROUP

Date of Inspection: 03.02.2025

Item	Identification Number	Description	W.L.L. Or D.O.W	Location	Inspection Date	Inspection Due	Comments	P / F / R / N
1	BB37225	FRANNA HOOK	14 TONNE	941	03.02.2025	FEB 2026	N/A	Pass
2	BB37478	FRANNA HOOK	25 TONNE	941	03.02.2025	FEB 2026	N/A	Pass
3	3514Y	13MM GRADE 100 2 LEG ASSEMBLY COMPLETE WITH MASTER LINK, CLEVIS GRABS AND CLEVIS SELF LOCKING HOOKS AT BASE. 6M	11.2 TONNE @ 60 DEG	941	03.02.2025	FEB 2026	N/A	Pass
4	3513Y	13MM GRADE 100 2 LEG ASSEMBLY COMPLETE WITH MASTER LINK, CLEVIS GRABS AND CLEVIS SELF LOCKING HOOKS AT BASE. 6M	11.2 TONNE @ 60 DEG	941	03.02.2025	FEB 2026	N/A	Pass
5	P2097	10MM GRADE 100 2 LEG ASSEMBLY COMPLETE WITH REGULAR MULTI LINK, EYE TYPE GRAB HOOKS AND CLEVIS SELF LOCKING HOOKS AT BASE. 8M	6.9 TONNE @ 60 DEG	941	03.02.2025	FEB 2026	N/A	Pass
6	P2022	10MM GRADE 100 2 LEG ASSEMBLY COMPLETE WITH REGULAR MULTI LINK, EYE TYPE GRAB HOOKS AND CLEVIS SELF LOCKING HOOKS AT BASE. 8M	6.9 TONNE @ 60 DEG	941	03.02.2025	FEB 2026	N/A	Pass
7	312	8MM GRADE 80 2 LEG ASSEMBLY COMPLETE WITH OBLONG LINK, EYE TYPE GRAB HOOKS AND CLEVIS SELF LOCKING HOOKS AT BASE.	3.5 TONNE @ 60 DEG	941	03.02.2025	FEB 2026	N/A	Pass
8	F2984	8MM GRADE 80 2 LEG ASSEMBLY COMPLETE WITH OBLONG LINK, EYE TYPE GRAB HOOKS AND CLEVIS SELF LOCKING HOOKS AT BASE.	3.5 TONNE @ 60 DEG	941	03.02.2025	FEB 2026	N/A	Pass
9	844	16MM GRADE 80 SINGLE LEG ASSEMBLY COMPLETE WITH OBLONG LINK AND CLEVIS SELF LOCKING HOOKS AT BASE. 2M	8 TONNE	941	03.02.2025	FEB 2026	N/A	Pass

1300 666 733 • www.allifting.com.au

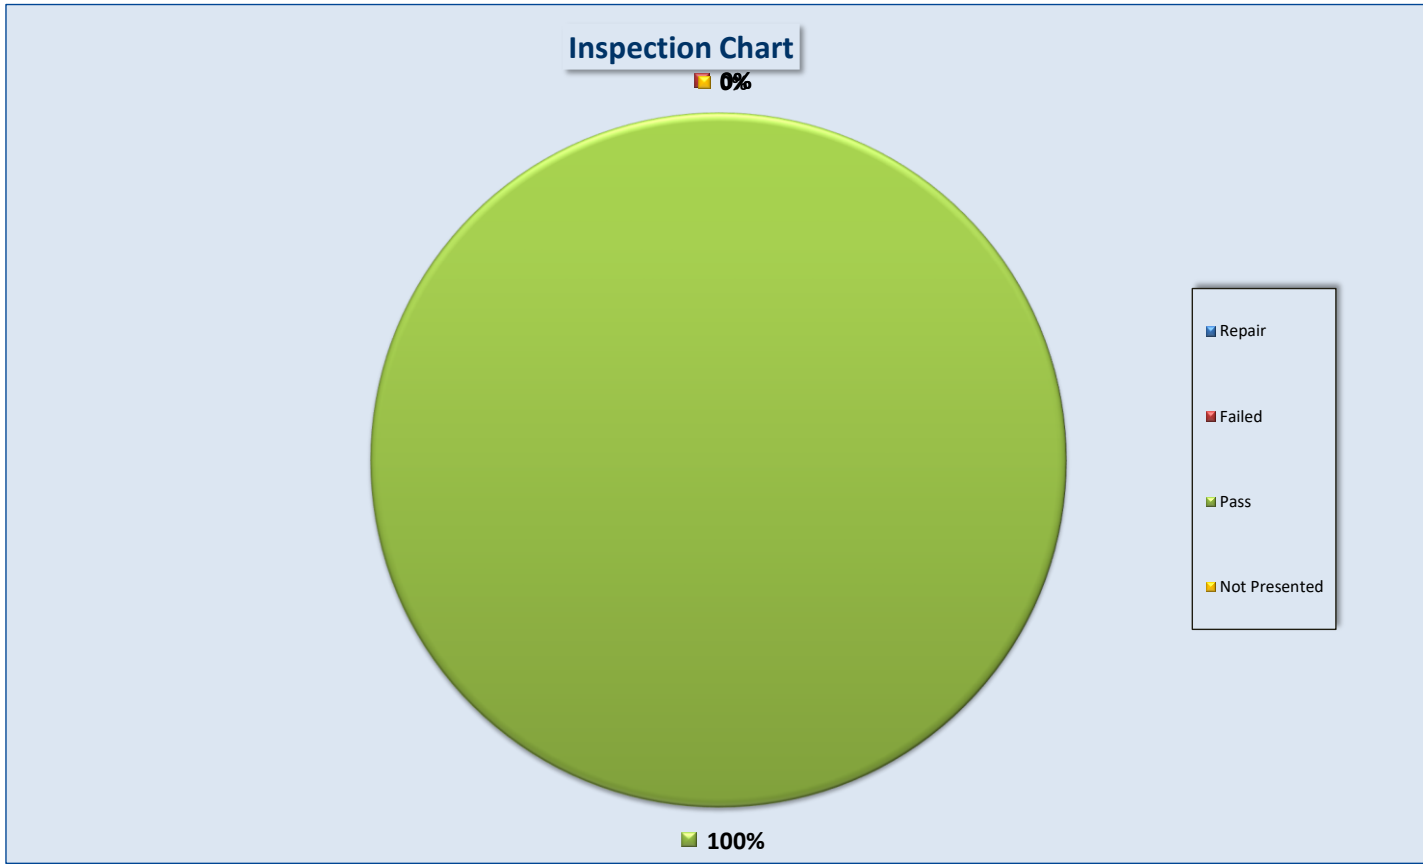

Report No:222183	
Repair	
Failed	
Pass	9
Not Presented	
TOTAL	9
