



Full Member



ABN 48 795 006 590

1/177 Power St, Glendenning, NSW, 2761
Phone: (02) 9838 4735



Full Member

VISUAL INSPECTION REPORT

Customer:	RAR CRANES AUSTRALIA	Contact:	ANDREW BODMAN
Location:	CHAINS	Inspection Date:	09/02/2026
D/D No:	N/A	Report No:	258654/UNIT 970
Report Received by:	andrewb@rargroup.com.au	Customer O/N:	N/A
Next Inspection Due:	FEBRUARY 2027	Colour Code:	RED

This report follows the visual inspection of lifting gear performed by Hasan Ozbal. Inspections were conducted with reference to Company endorsed Work Instructions, Relevant Standards, Occupational Health & Safety requirements and Manufacturers recommendations to determine acceptance / rejection criteria's.

1. AS 3775.2:2014 Chain slings for lifting purposes - grade T(80) and V(100) product specification
2. AS 3850.1 Clause 2.6 Prefabricated concrete elements general requirements
3. AS 3776 :2015 Lifting components for grade T(80) and V(100) chain slings
4. AS 4991-2004 Lifting Devices

All items satisfying the above requirements were tagged or hard stamped to cross reference with this report.

Items listed as "R" (Repair) should be quarantined and repaired prior to further use.

Items listed as "F" (Failed) are not suitable for continued use or for their intended purpose and should be destroyed and discarded immediately. We cannot accept any responsibility for continued use.

Items listed as "N" (Not Presented) were unable to be located on site.

Items listed as "P" (Pass) are suitable for continued use and can be put back into service. Should any replacement parts be required they can be supplied by reference to the item number of this report.

All items have been fitted with a RED colour coded identification tag. We shall contact you early February 2027 to arrange your next inspection. Should you require any further information please contact the undersigned.

Yours Truly

Hasan Ozbal
Inspection Officer
Email: hasano@alllifting.com.au
Mobile: 0403 208 495
Phone: (02) 9838 4735

1300 666 733 • www.alllifting.com.au



Full Member



ABN 48 795 006 590

1/177 Power St, Glendenning, NSW, 2761
Phone: (02) 9838 4735



Full Member

Report: 258654/UNIT 970

Customer: RAR CRANES AUSTRALIA

Date of Inspection: 09/02/2026

Item	ID Number	Description	W.L.L.	D.O.W.	Location	Insp. Date	Insp. Due	Comments	P/F/R/N
1	J709	CHAIN SLING 10MM 2 LEG GR-120 C/W MULTI HEAD RING EYE GRAB HOOK/S CLEVIS SELF LOCKING HOOK/S 8MTR	8.45 TONNE @ 60°	N/A	UNIT 970	09/02/2026	02/2027	TRIGGER REPAIR	Pass
2	J710	CHAIN SLING 10MM 2 LEG GR-120 C/W MULTI HEAD RING EYE GRAB HOOK/S CLEVIS SELF LOCKING HOOK/S 8MTR	8.45 TONNE @ 60°	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
3	E946	CHAIN SLING 16MM 2 LEG GR-100 C/W MULTI HEAD RING EYE GRAB HOOK/S CLEVIS SELF LOCKING HOOK/S 8MTR	17.3 TONNE @ 60°	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
4	E947	CHAIN SLING 16MM 2 LEG GR-100 C/W MULTI HEAD RING EYE GRAB HOOK/S CLEVIS SELF LOCKING HOOK/S 8MTR	17.3 TONNE @ 60°	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
5	5B 73	CONCRETE CLUTCH MUSHROOM TYPE - AR	2.5 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
6	818	CONCRETE CLUTCH MUSHROOM TYPE - AR	2.5 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
7	PH-0584-11	CONCRETE CLUTCH MUSHROOM TYPE - PHILLIPS	2.5 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
8	7G 24	CONCRETE CLUTCH MUSHROOM TYPE - SWIFTLIFT	2.5 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
9	6F 839	CONCRETE CLUTCH MUSHROOM TYPE - SWIFTLIFT	5 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
10	6F 92	CONCRETE CLUTCH MUSHROOM TYPE - SWIFTLIFT	5 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
11	9F 467	CONCRETE CLUTCH MUSHROOM TYPE - SWIFTLIFT	5 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
12	9F 484	CONCRETE CLUTCH MUSHROOM TYPE - SWIFTLIFT	5 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
13	KAWDR L	CONTAINER HOOK LEFT - YOKE	12.5 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
14	KAWDR L	CONTAINER HOOK LEFT - YOKE	12.5 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
15	KAWWW R	CONTAINER HOOK RIGHT - YOKE	12.5 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
16	KAWWW R	CONTAINER HOOK RIGHT - YOKE	12.5 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
17	BB39815	HOOK ASSEMBLY FRANNA HOOK	14 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
18	BB40460	HOOK ASSEMBLY FRANNA HOOK	25 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass
19	150005-04	LIFTING DEVICE COMBINATION BEAM FRANNA COMBO BEAM	15 TONNE	N/A	UNIT 970	09/02/2026	02/2027	N/A	Pass

1300 666 733 • www.alllifting.com.au



Full Member



ABN 48 795 006 590


1/177 Power St, Glendenning, NSW, 2761
Phone: (02) 9838 4735



Full Member

Inspection Chart

Repair Fail No Presented Pass

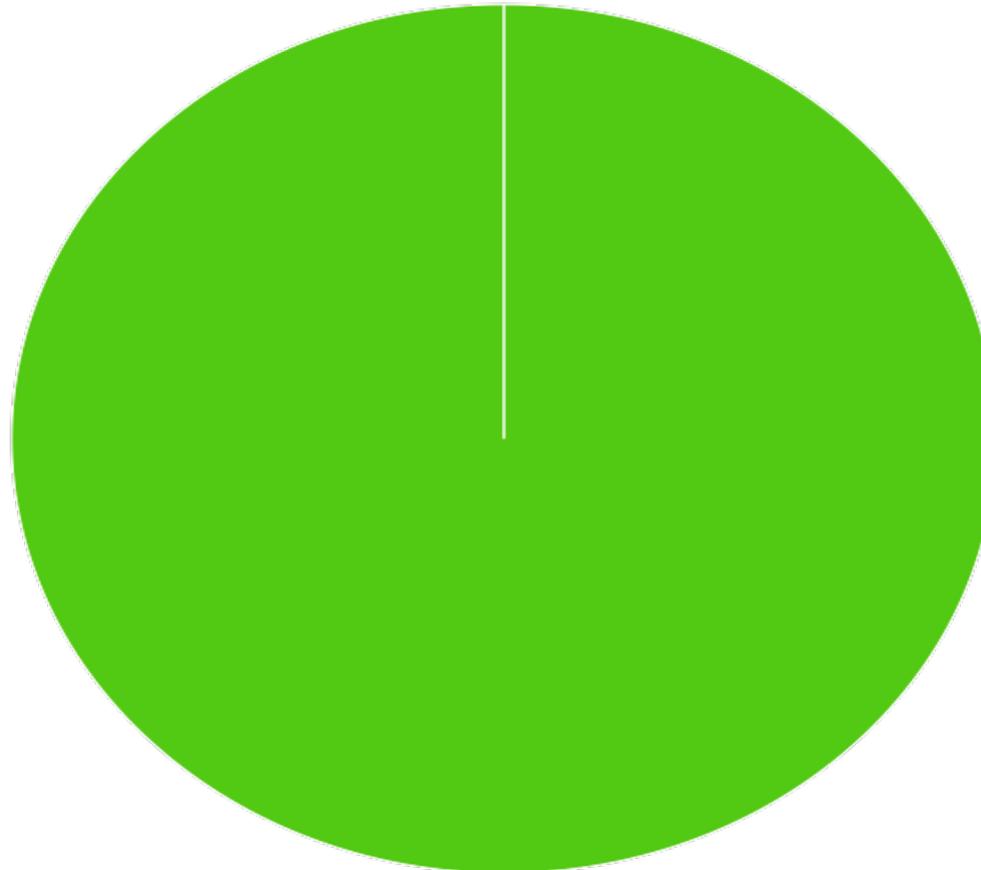

Report No	258654/UNIT 970
Repair	0
Not Presented	0
Pass	19
Failed	0
TOTAL	19

1300 666 733 • www.alllifting.com.au
